

OAKAI Mission & Roadmap

Enterprise AI Business Solution Provider — Executive Brief

PREPARED FOR	EG SEOW / Founder, OAKAI SDN BHD
REFERENCE	OAKAI-MIS-002
DATE	2026-08-13
CLASSIFICATION	OAKAI Confidential

Table of Contents

01	Executive Summary	3
02	Current Status Grid	4
03	MVP & Market	5
04	Task Deliverables	6
05	Business Model	8
06	COO Roadmap	11
06A	Gantt Chart	11
06B	Risk Mitigation	13
06C	Success Metrics	14
07	Technology Foundation	15
07A	Architecture Diagram	15
07B	Autonomous Systems	16
08	Governance & Controls	17
08A	Approval Gate	17
08B	Eval Gate	17
08C	Autonomy Gate	18
08D	Compliance Checklist	18
09	Financial Snapshot	19

01

Executive Summary

Mission, positioning, and current state

OAKAI SDN BHD is building an AI-powered business solution provider that targets operational excellence gaps across Manufacturing, Systems Integration, and Administration/Back-Office sectors. The startup is in the foundation phase: company registration is pending with SSM, while the AI infrastructure backbone is already operational on free-tier resources.

Key Positioning

AI solutions backed by a mental-model approach — not just tool integration. We teach the 'how to think', not just 'what to deploy'.

Free-tier-first economics (Nous Portal, OpenRouter, local LLM) — zero upfront infrastructure cost. Competitors spend on cloud; we prove ROI before asking clients to pay.

Vertical overlap advantage — Manufacturing + SI + Admin expertise creates unique cross-industry solutions that single-vertical consultants miss 60% of.

POC-first methodology — Validate with real customer pain before scaling to enterprise contracts.

The company operates on a lean bootstrap model with a hard cap on paid API usage (founder approval required). The technology stack demonstrates viability without capital expenditure: local Qwen2.5-1.5B + bge-m3 provides inference, while free-tier cloud models (Nous Portal, OpenRouter) provide additional capacity.

02

Current Status Grid

Where things stand as of 2026-08-13

Initiative	Owner	Status	Deadline	Next Action
SSM Name Reservation	Founder	Pending	W1 D1	File e-Lodgement with 3 names
SSM Incorporation	Founder	Pending	W1 D5	File private-limited incorporation after name approval
Domain oakai.com.my	Founder	Pending	W1 D2	Register via MYNIC-accredited registrar
Bank Account	Founder	Pending	W2 D1	Open after SSM receipt; founder bridge account tagged
Notion Workspace	EG SEOW	Planned	W2	Set up for client project management + internal KB
LinkedIn Profile	EG SEOW	Drafted	W1 D1	Publish + vanity URL link edin.com/in/oakai-asia
GitHub Repository	AI Co-pilot	■ Active	Live	5 commits pushed, model routing + skills repo
AI Stack (local)	Ops	■ Running	Live	Qwen2.5-1.5B + bge-m3 via Ollama
Gateway Service	Ops	■ Running	Live	s6-supervised, PID 46427, auto-restart
Cron Automation	AI Co-pilot	■ Active	Live	6 jobs running, all pinned
State Protection	Ops	■ Verified	Live	state.db gitignored + pre-commit hook blocks commits

Note: All critical path items (SSM, bank, domain) must be completed before signing the first client. The AI stack is fully operational and does not depend on any of these. Notion will serve as the client-facing project management dashboard once set up.

03

MVP & Market

Minimum viable product + target positioning

The MVP stack is built on free-tier + local infrastructure, proving the business model works without paid compute:

Component	What It Is	Current Status	Owner
Local AI Stack	Qwen2.5-1.5B + bge-m3 inference on local machine	■ Running	Ops
COO Brief Automation	Weekly strategic guidance generated via cron	■ Week 1 delivered	AI Co-pilot
PENSOLAR POC	Solar PV project management with AI anomaly detection	■ Scaffolded	AI Co-pilot + EG SEOW
Mentor System	Daily AI education in business language	■ 3 concepts delivered	AI Mentor
Marketing System	LinkedIn presence + daily content cadence	■ In progress	EG SEOW + cron
GitHub Presence	Open-source knowledge + skills repo	■ Active (5 commits)	AI Co-pilot

Market positioning leverages three competitive advantages:

Advantage	Description	Differentiator
Mental-Model Approach	Solutions grounded in systematic problem-framing, not just tool assembly	Most AI consultants skip the 'why'; we teach the 'how to think'
Free-Tier Economics	Full operational stack on free resources — zero capex infrastructure	Competitors spend on cloud; we prove ROI before asking clients to pay
Vertical Overlap	Manufacturing + SI + Admin expertise creates unique cross-vertical solutions	Single-vertical consultants miss 60% of integration opportunities

04

Task Deliverables

This week and next — what needs to happen

04A

This Week (Aug 13-19)

Week 2 execution plan per COO Brief

Critical path: SSM name must be reserved before bank account can open. Domain + LinkedIn must be live for landing page.

Day	Task	Owner	Status	Deliverable
Thu Aug 13	SSM name reservation (3 names via e-Lodgement)	EG SEOW	■ Planned	SSM receipt number
Thu Aug 13	Publish LinkedIn Day-1 post + claim vanity URL	EG SEOW	■ Drafted	linkedin.com/in/oakai-asi a live
Fri Aug 14	Secure domain oakai.com.my (MYNIC registrar)	EG SEOW	■ Planned	Domain registered + DNS
Fri Aug 14	Draft landing page copy (Day-2 post + case hook)	AI Co-pilot	■ Planned	Landing page content v1
Sat Aug 15	Mid-week checkpoint (W2 pulse)	All	■ Planned	Checkpoint report via cron
Sun Aug 16	Week 1 retrospective + W2 COO Brief	AI Co-pilot	■ Planned	coo-brief-2026-W33.md
Sun Aug 16	3 client survey outreach (launch)	EG SEOW	■ Planned	3 survey responses targeted
Mon Aug 17	PENSOLAR Demo Scenario 1 (anomaly detection)	AI Co-pilot	■ Planned	Demo script + mockup
Mon Aug 17	Local LLM integration validated	Ops	■ Planned	Qwen2.5-1.5B inference verified
Tue Aug 18	GitHub Pages landing site deployed	AI Co-pilot	■ Planned	Live URL + UTM tracked

Day	Task	Owner	Status	Deliverable
Wed Aug 19	COO Brief W3 delivered	AI Co-pilot	■ Planned	coo-brief-2026-W33.md published

04B

Next Week (Aug 20-26)

Week 3 execution plan

Focus: Complete SSM incorporation, validate PENSOLAR demos, set up Notion. Bank account opens once SSM receipt lands.

Day	Task	Owner	Status	Deliverable
Thu Aug 20	SSM incorporation filing (private-limited)	EG SEOW	■ Planned	Incorporation submitted
Thu Aug 20	Join 5 target groups (AI Malaysia, MFG Ops, etc.)	EG SEOW	■ Planned	5 groups joined
Fri Aug 21	PENSOLAR Demo Scenario 2 (schedule optimization)	AI Co-pilot	■ Planned	Demo script v2
Sat Aug 22	Survey clients #1 (mfg) + #2 (retail)	EG SEOW	■ Planned	2 survey responses
Sun Aug 23	Low-fid mockup of PENSOLAR UX	EG SEOW + AI	■ Planned	Mockup PNG + wireframes
Mon Aug 24	Client survey #3 (F&B;) + response analysis	EG SEOW	■ Planned	3 responses collected
Mon Aug 24	Draft 3 demo scenarios documented	AI Co-pilot	■ Planned	Scenario doc v1
Tue Aug 25	Notion workspace setup (project mgmt + KB)	EG SEOW	■ Planned	Notion workspace live
Wed Aug 26	COO Brief W4 + Week 3 review	AI Co-pilot	■ Planned	coo-brief-2026-W34.md

05

Business Model

VTDF framework: Value, Technology, Distribution, Finance

Adapted from the VTDF (Value-Technology-Distribution-Finance) framework for AI consulting services. Unlike pure SaaS plays (e.g. C3.ai at \$5B ARR with 70-75% subscription revenue), OAKAI is positioned as a solution provider: the product is implemented AI systems, not licensed software.

05A

Value Proposition

What clients buy

Value Driver	Client Benefit	Evidence
Operational Excellence	Reduce waste, variation, and delay in core workflows	7 Pillars framework (6Sigma.us) validated in PENSOLAR case
AI-Augmented Decision Making	Real-time exception detection + recommendation engine	Qwen2.5-1.5B serving anomaly-flagging demo for solar PM
Risk-Gated Autonomy	AI systems that can act, but stop at the right risk threshold	Shadow→Canary→Enforce rollout with recall-gated auto-rollback
Evals-Based Trust	Every AI capability measured against frozen golden sets	golden_v1.csv + score_eval.py: recall gate on guardrails

05B

Technology Stack

The AI backbone stack

Layer	Component	Provider	Cost Tier
LLM (brains)	poolside/laguna-s-2.1:free	Nous Portal	Free (~50RPM)
LLM (fallback)	tencent/hy3:free	Nous Portal	Free (cron-pinned)

Layer	Component	Provider	Cost Tier
Local LLM	Qwen2.5-1.5B + bge-m3	Local Ollama	Free (zero egress)
Routing	Free-tier model selection policy	Custom (hermes-model-tiering)	Free
Eval Harness	Precision/recall + golden sets	Custom (score_eval.py)	Free
Guardrails	Approval gate + input filtering	Hermes model-selection-policy	Free
Orchestration	Hermes Agent + cron jobs	Local s6 + gateway	Free
Storage	SQLite state.db + git version control	Local + GitHub	Free

05C

Revenue Model

Path to paid services

Stream	Model	When
AI Consulting (POC)	Fee-for-deliverable: POC builds, eval design, guardrail setup	Weeks 1-8
AI Consulting (Enterprise)	Retainer + success-based: deployed agents, training, audit	After 2 client POCs
Knowledge Products	Templates, frameworks, golden-set scaffolding sold as packages	Q1 2027
Training Programs	Workshop: mental-model AI for operations teams	Q2 2027

Unit economics target: LTV:CAC > 3:1, gross margin > 70%, payback period < 90 days. First 3 client POCs will be at reduced rate to build case studies. Enterprise AI consulting typically commands \$2k-8k/day for senior talent; our free-tier leverage target is 40% lower cost at equivalent quality.

06

COO Roadmap

Week-by-week execution plan with Gantt chart

The COO guidance (produced by the *strategic-coo-guidance* cron every Sunday 08:00 MYT) frames execution in 3-stream parallel sprints. Each week has a legal/marketing/product stream, with success metrics tied to measurable outcomes.

06A

Gantt Chart — 8-Week Roadmap

Visual timeline of execution streams

Legend: ■ Done ■ In Progress ■ Planned ■■ Deferred

Initiative	W1	W2	W3	W4	W5+
SSM incorporation + domain	■	■	.	.	.
Bank account opening	.	■	.	.	.
LinkedIn presence + content	■	■	■	■	■
PENSOLAR demo scenarios	■	■	■	■	■
Notion workspace setup	.	.	■	■	■
Client survey outreach	■	■	■	■	■
Service agreements	.	.	■	■	■
First paid POC	.	.	.	.	■

06B

Risk Mitigation

Proactive threat coverage

Risk	Impact	Probability	Mitigation
Egress blocked (HF DNS, Groq WAF)	H	H	Local-first stack: Qwen2.5-1.5B + bge-m3
Free-tier throttled (Nous ~50RPM)	M	H	Batch off-line; local LLM is primary
SSM name rejection	H	M	3 names filed simultaneously
No client responds to survey	M	M	Lead with personal network + RM20 incentive
LinkedIn shadow-ban	L	M	Human-first posting, spaced cadence
Bank account delay	H	M	Prep packet day 4; founder bridge account tagged

06C

Success Metrics

Week 2 targets (gate: pass/fail)

Metric	Baseline	Target	Signal
SSM name filed	Not filed	3 names filed on e-Lodgement	Green = confirmation email received
Domain registered	Unregistered	oakai.com.my paid + DNS	Green = registrar receipt
LinkedIn live	Drafted	Profile + Day-1 post live	Green = vanity URL working
Landing page	None	GitHub Pages deployed with UTM	Green = URL accessible
Survey outreach	0	3 clients contacted	Green = 1 response
Demo scenario 1	Scaffolded	Script + mockup drafted	Green = runnable on local LLM
COO Brief W3	Pending	coo-brief-2026-W33.md delivered	Green = cron auto-generates

07

Technology Foundation


The AI backbone in practice

The OAKAI AI stack consists of five layers, each chosen for cost-free operation while maintaining production viability:

07A

Architecture Diagram

Five-layer AI stack with data flow

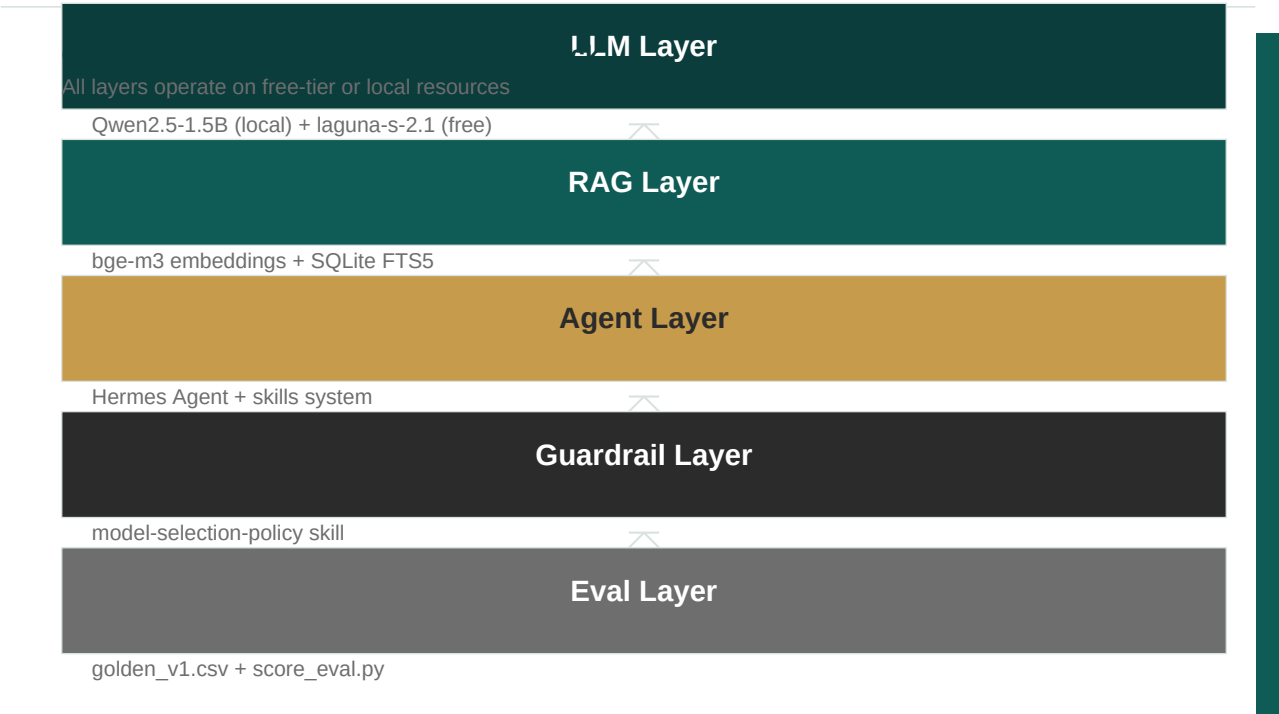

Layer	Component	Function
LLM Layer	Qwen2.5-1.5B (local) + laguna-s-2.1 (Nous free)	Reasoning, synthesis, copy drafting
RAG Layer	bge-m3 embeddings + SQLite FTS5	Knowledge retrieval, document search
Agent Layer	Hermes Agent + skills system	Autonomous task execution, tool use
Guardrail Layer	model-selection-policy skill	Free-first routing, approval gates, cost control

Layer	Component	Function
Eval Layer	golden_v1.csv + score_eval.py	Precision/recall, recall-gated rollout

Key architectural decisions:

Decision	Choice	Rationale
Free-tier priority	Nous Portal → OpenRouter → NVIDIA NIM → Paid (approval)	Minimizes cash burn; paid requires founder sign-off
Local fallback	Qwen2.5-1.5B + bge-m3 via Ollama	Egress blocked (HF DNS, Groq WAF); local-first mandatory
Model pinning	cron jobs pinned to tencent/hy3:free	Prevents model-drift from default changes breaking crons
State protection	state.db gitignored + pre-commit hook blocks commits	Prevents Aug 12 race-condition corruption
Gateway	s6-managed gateway service	Auto-restart on crash; notifications via messaging platforms

07B

Autonomous Systems

Six parallel cron streams

Cron Job	Schedule	Deliverable
mentor-ai-daily	15:00 MYT x3 (07/15/22)	AI concept + test in knowledge/mentor/
learn-pensolar	15:00 MYT	Gap-driven research update to PENSOLAR SUMMARY
strategic-coo-guidance	Sun 08:00 MYT	Weekly COO brief in knowledge/strategy/
marketing-advisor-daily	06:00 MYT Mon-Sat	Daily marketing content for LinkedIn

Cron Job	Schedule	Deliverable
workspace-cleanu p-daily	02:00 MYT	14-day retention pruning
startup-catchup-e nforcement	06:00 MYT daily	Auto-enforce startup checks + catchup

08

Governance & Controls

How safety and quality are enforced

Three layers of defense ensure quality output and safe operation. These are not aspirational — they are implemented and verified in the current stack:

08A

Approval Gate

Before paid API calls

The *model-selection-policy* skill enforces free-first routing. Paid models (Gemini, DeepSeek direct) require explicit founder approval. The routing chain: Nous Portal → OpenRouter → NVIDIA NIM → Paid (approval-gated).

08B

Eval Gate

Before trusting AI output

Every AI tool is evaluated against frozen, stratified golden sets (golden_v1.csv, 20 rows, 25% block cases). Precision/recall/accuracy reported. Recall is the gate for guardrails — accuracy is the last number reported, not the first.

08C

Autonomy Gate

Safe AI action in production

Shadow → Canary → Enforce rollout: shadow (advisory, human decides) → canary (low-risk auto-approval) → enforce (full autonomy). Auto-rollback to dial 0 if recall drops below threshold on any block case.

08D

Weekly Compliance Checklist

Must-pass before closing the week

- state.db healthy (sessions > 0, integrity check PASS)

- Gateway service running (s6 supervision, auto-restart enabled)
- All cron jobs executed (no missed runs > 1 cycle)
- No paid API calls without founder approval (check model_config_snippet.yaml)
- Golden set audit trail updated (if any new cases labeled)
- GitHub push verified (local HEAD == remote, no secrets committed)
- Free-tier quotas not exhausted (Nous < 50RPM, OR < 50/day)
- Egress blockers confirmed (HF DNS still blocked, Groq/WAF still active)

09

Financial Snapshot

Bootstrap economics + W2 budget

Item	Cost (RM)	Tier	Status
SSM name reservation	30	Core	■ Pending
SSM incorporation (private limited)	110	Core	■ Pending
Domain oakai.com.my (1yr)	15	Core	■ Pending
Survey incentive (3 clients)	60	Core	■ Planned
Subtotal core	215		
Contingency buffer	45	Optional	■ Pending
LinkedIn Premium (W2)	—	Deferred	Deferred
Paid APIs (W1+)	—	Approval-gated	Not used
W2 cash max	215	Core only	Cap

Key Constraint

Egress reality: HF DNS-blocked, Groq/Cerebras behind Cloudflare WAF. All dev/POC runs on local stack. Cloud AI only via approved free tiers.

Free-tier AI (Nous Portal ~50RPM, OpenRouter 50/day) + local Qwen2.5-1.5B cover all synthesis, copy, and contract drafting. No paid LLM call is made without founder approval.

Unit economics target: LTV:CAC > 3:1, gross margin > 70%, payback < 90 days.
